



State Project ID: 5954-00-01  
CTH M  
Oncken Rd to STH 113  
Dane County

Update Date: May 3, 2024

## Project Weekly Update (CTH M Construction)

### General Project Information –

The reconstruction of CTH M includes reconstructing its current two-lane traffic configuration to a four-lane divided traffic configuration with grass medians. CTH M will have two lanes in each direction from approximately Oncken Rd to STH 113. The project includes removals, excavations, base aggregate, HMA pavement, concrete curb and gutter, concrete sidewalk, structures, culvert pipe, storm sewer, MGS guardrail, temporary shoring, erosion control, traffic control, restoration, pavement marking, permanent signing, street lighting, temporary and permanent traffic signals, ITS, and structure work for B-13-439, B-13-601, B-13-895. The overall work is scheduled for completion in November 2024.

### Project Schedule:

- Overall Completion Date: November 30, 2024

Current Stage / Traffic Impacts: STAGE 2 - work consists of mainline excavation of CTH M, storm sewer installation on CTH M, boardwalk extension construction, and construction of the new bridge structure B-13-895. Road work will also take place on the sideroads located throughout the project corridor.

- Private utilities continue to work throughout the CTH M corridor relocating facilities for the roadway project.
- CTH M and CTH K will remain open to traffic, however, flagging operations maybe present on any given day.
- The multi-use path from North Shore Bay Drive to Woodland Drive and up Woodland Drive to the Carriage Ridge Conservancy Park will remain closed until further notice.
- Mary Lake Road is anticipated to close to traffic from the CTH M intersection to the first Westport Town Hall driveway on May 13, 2024 at 5:00 AM and will be closed for approximately 15 days, see closure map below.

### Work this week (week of 5/6/2024)

- Crews will maintain traffic control devices.
- Crews will continue survey and layout operations.
- Crews will continue off alignment topsoil removal operations.
- Crews will continue asphalt pavement removals, roadway common excavation, and aggregate placement as necessary.
- Crews will continue storm sewer installation throughout the corridor.




### Work scheduled for the next week (week of 5/13/2024)

- Crews will maintain traffic control devices.
- Crews will continue survey and layout operations.
- Crews will continue asphalt pavement removals, roadway common excavation, and aggregate placement as necessary.
- Crews will continue storm sewer installation within the Stage 2 work limits.
- Crews will begin reconstructing Mary Lake Rd at CTH M.



Grading operations for the new North Shore Bay Drive configuration.

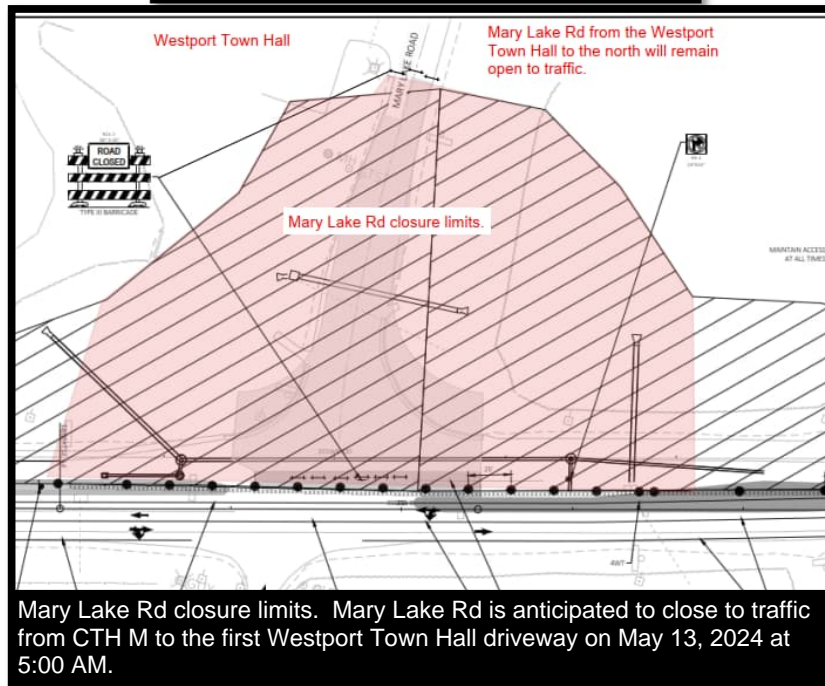

Mary Lake Rd closure limits. Mary Lake Rd is anticipated to close to traffic from CTH M to the first Westport Town Hall driveway on May 13, 2024 at 5:00 AM.

Please be alert when traveling the CTH M corridor. Please note that work is weather dependent and may be subject to change. The use of the alternate route is recommended, see attached map below. Thank you to everyone for your continued patience and understanding throughout the construction season.



### Contact information

Trenton Diehl, Strand Associates, Inc. - Project Leader

Email: [trenton.diehl@strand.com](mailto:trenton.diehl@strand.com)

If you would like to be added or removed from the weekly update distribution list, please email your name and email address to [trenton.diehl@strand.com](mailto:trenton.diehl@strand.com).

### Project Website

<https://highway-projects-countyofdane.hub.arcgis.com/pages/cth-m>

## CTH M Construction Alternate Route

